BRUHAT BENGALURU M

	Clients Name		Executive Engineer Byatarayanapua Division
	Project Name	:	Package - 4 includes 4 works of Rs.195.00 lakhs 1).Improvements to roa surrounding areas in Ward No.07, Byatarayanapura. 3).Improvements to Byatararayanapura in Ward No.07, Byatarayanapura
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	31-Oct-18
	Project End Date	:	28-Feb-19
	Project Length in Months	:	4 months

Sl. No	*Assignment*	*Unit*	*Boq Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Earth work excavation by manual means in ordinary soil involving an average horizontal throw upto 2 meters and an average lift upto 0.5m, excavated	Cum	2376.65	1746.50	73	31-10-18	28-02-19	120
2	Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2meters and an average lift upto 1.5 m, excavated	Cum	857.02	431.91	50	02-11-18	28-02-19	118
3	Removing & Refixing stone slabs and drains and Pointing in and as per the direction of Engineer in charge of the work.	Sqm	498.96	760.05	100	02-11-18	28-02-19	118
4	Providing granite 7.5cms thick slabs of selected quality roughly dressed and fixed in cement mortar(1:6)	Sqm	295.44	316.85	100	03-11-18	28-02-19	117
5	Providing and laying in position Plain cement concrete of mix 1:4:8	Cum	1015.20	844.52	83	03-11-18	28-02-19	117
6	Providing and laying in position Plain cement concrete of mix 1:2:4	Cum	16.38	27.23	100	05-11-18	28-02-19	115
7	Providing and constructing granite/trap/basalt size stone masonry in foundation in CM 1:6	Cum	31.59	101.52	100	03-11-18	28-02-19	117
8	Providing and constructing granite/trap/basalt size stone masonry in superstructure with cement mortar **b) With available stones**	Cum	28.35	40.59	100	04-11-18	28-02-19	116
9	Providing ruled pointing of course stone masonry with cement mortar 1:3	Sqm	238.20	793.80	100	04-11-18	28-02-19	116
10	Cement concrete pavement. Constructionn of un reinforced plain cement concrete pavement, thickness as per design	Cum	731.75	562.85	77	05-11-18	28-02-19	115
11	Vaccume de-watering with vaccum pump and suction mat and compaction with skin floater	Sqm	4898.50	5628.47	100	05-11-18	28-02-19	115
12	Providing,laying, spreading and compacting crushed stone aggregates of granite/trap/ basalt to wet mix macadam	Cum	237.00	198.83	84	07-11-18	28-02-19	113
13	Providing and applying primer coat with S.S. bitumen emulsion on prepared surface	Sqm	1185.00	994.17	84	13-11-18	28-02-19	107
14	Providing and laying bituminous concrete 40mm	Cum	47.40	39.77	84	13-11-18	28-02-19	107

IAHANAGARA PALIKE

ls and drains near Hebbal Shanimahatma temple in Ward No.07, Byatarayanapura. 2).Improvements to roads and drains Amruthalli gramatana pending works and oads and drains Sanjeevinagara, Byatarayanapura and Kempapura in Ward No.07, Byatarayanapura. 4).Improvements to drains Hoysala Apartment towards

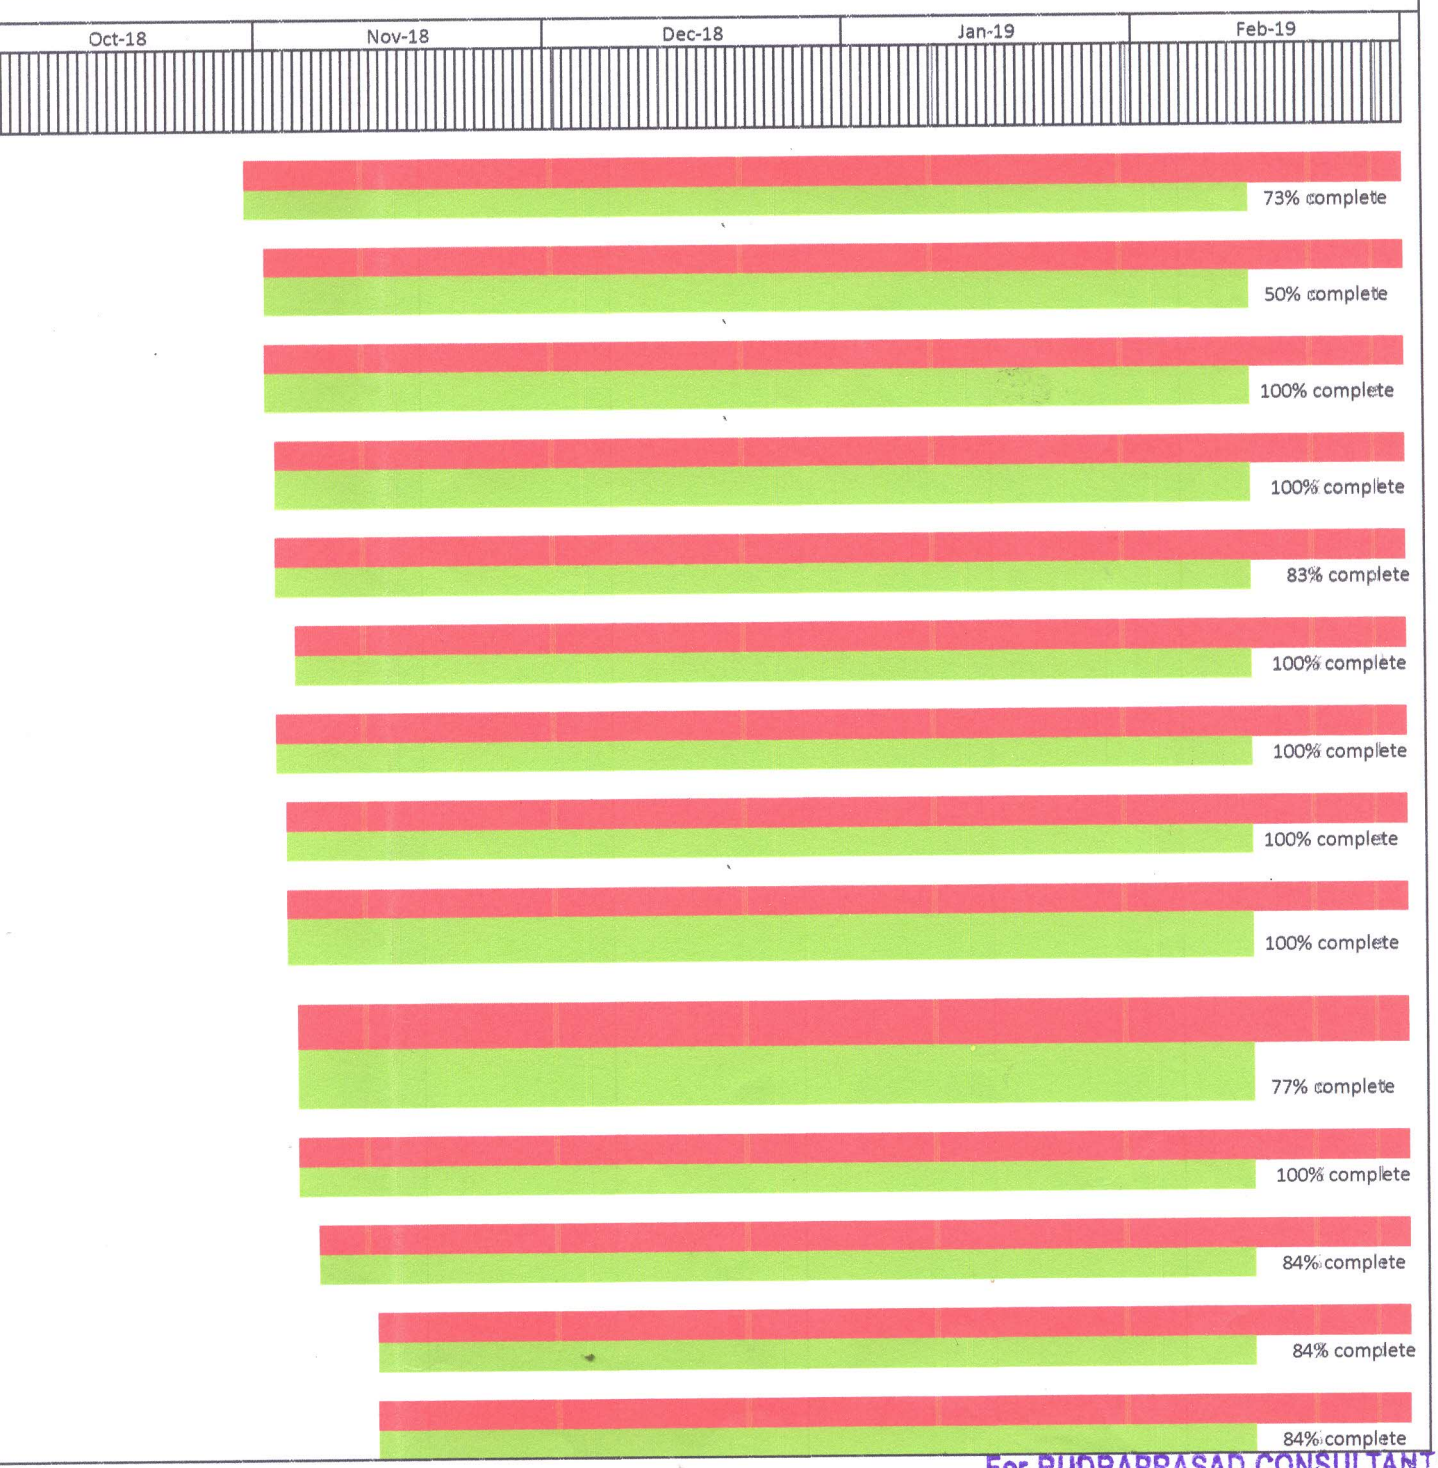

For RUDRAPRASAD CONSULTANTS

Partner./s.

7

BRUHAT BENGALURU M

	Clients Name		Executive Engineer Byatarayanapua Division
	Project Name	:	Package - 4 includes 4 works of Rs.195.00 lakhs 1).Improvements to road surrounding areas in Ward No.07, Byatarayanapura. 3).Improvements to r Byatararayanapura in Ward No.07, Byatarayanapura
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	31-Oct-18
	Project End Date	:	28-Feb-19
	Project Length in Months	:	4 months

Sl. No	*Assignment*	*Unit*	*Boq Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
15	Providing and laying in position reinforced cement concrete	Cum	80.10	0.00	0	16-11-18	28-02-19	104
16	Providing TMT Steel Reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever	Tonne	48.06	0.00	0	12-11-18	28-02-19	108
17	Providing and removing Centering, shuttering, strutting, propping etc	Sqm	640.80	0.00	0	18-11-18	28-02-19	102
18	Loading and unloading of stone boulder/stone aggregates/ sand/ kanker/ moorum.	Sqm	3160.77	1679.43	53	31-10-18	28-02-19	120

Asst Exe. Engg
AE(121)

Assistant Executive Engineer
Kodigehalli Sub Division
Bruhat Bangalore Mahanagara Pali
Bangalore - 560 092

AHANAGARA PALIKE

and drains near Hebbal Shanimahatma temple in Ward No.07, Byatarayanapura. 2).Improvements to roads and drains Amruthalli gramatana pending works and ads and drains Sanjeevinagara, Byatarayanapura and Kempapura in Ward No.07, Byatarayanapura. 4).Improvements to drains Hoysala Apartment towards

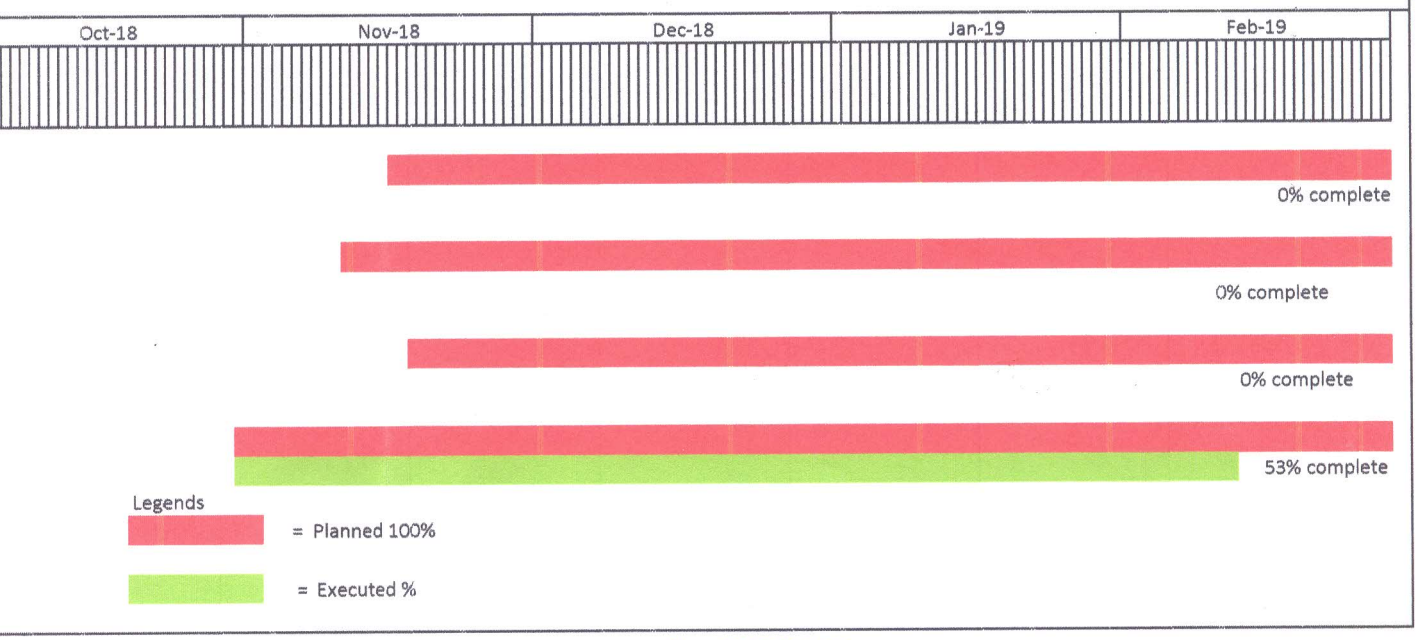

For RUDRAPRASAD CONSULTANTS

Partner./s.
